

**PROGRESS REPORT OF WORK ON GOING SCHEME/MORE THAN 200 LAKHS FOR THE MONTH OF OCTOBER -2017**

Name of Division	Name of work	Date of AA/ES	Date of Publishing Tender	Date of Award	Date of Start of work	Value of Award	Name of the contractor	Authority approving the contract	Final date of completion of project	Major Activities	Date of completion	Stage of completion	% of completion	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	14
EE(E) C-VI	<b>Deposit Work</b> Establishing two 33KV ESS at Kidwai Nagar Sub- Station work	Technical register at page No.05, Sr.No.23 on dt.19.08.15 for Rs.15,09,85,298/-	16.02.16	10.06.16	31.07.16	29,59,49,800/-	M/s. JSP Projects Pvt. Ltd.	Council item No.25(B-02) dt 26.04.16	-	33KV GIS boards, 11KV boards, 33KV Power, Transformers 11 KV Station Transformers & LT Boards.	30.05.17	-	75%	Supply of major equipment received at site. ITC work of equipments for ESS-I is in progress. ITC work of Equipments for ESS-II shall be started after completion of building of ESS-II which is being constructed by M/s. NBCC.
EE(E) C-VI	<b>Deposit Work</b> Establishing two 33KV ESS at Kidwai Nagar(East) SH: Supplying, Laying, Testing & Commissioning of 33KV, 400Sq.mm/3c, XLPE cable for 33KV ESS at Kidwai Nagar(East)	Technical register at page No.05, Sr.No-24 on dt.19.08.15 for Rs. 6,56,86,300/-	16.02.16	14.06.16	31.07.16	10,64,15,850/-	M/s. Universal Cables Ltd.	Council item No-24(B-01) dt.26.04.16	-	33KV HT Cable & its laying, testing & commissioning	30.05.17	-	80%	33 KV Cable received. Three feeders out of total 5 Nos.. feeders have been laid. Cable laying work stopped due non availability of cable trenches which was provided by M/S. NBCC
EE(E) C-VI	<b>Feeders work</b> Supply, Installation, Testing & Commissioning 66/11KV, 16/20MVA Power Transformers & 33/11 KV, 16/20 MVA Power Transformer at various ESS of NDMC	5(B-10) dt.27.08.2014 & 18(b-4) dt. 09.07.2014 Technical register at page No. 07, Sr.No. 30 on dt.05.09.16 for Rs.5,15,00,000/-	19.10.16	23.03.17	29.04.17	5,11,00,000/-	M/s. Capital Electech Pvt. Ltd.	Council item No-09(B-24) dt.16.01.17	-	SITC of 66/11 KV 16/20 MVA & 33/11 KV, 16/20 MVA Power Transformers	28.12.17	-	70%	All three power Transformer has been received at sites. Testing work of 66/11 KV PTR for Vidyt Bhawan & 33/11 KV PTR for Shahjahan Road is in Progress.

*Bhacqd*  
16/11/17  
EE(T-II)

*Omrah*  
Checked by Sr.Asstt (T-II)

*18*  
15/11/17  
Sr.Asstt. (T-II)

**PROGRESS REPORT OF WORKS ONGOING SCHEMES MORE THAN 200 LACS FOR THE MONTH OF OCTOBER 2017 IN (EC-VI) Division**

Name of Division	NAME OF WORK	Date of A/A/E/S	Date of Publishing Tender	Date of Award	Date of start of work	Value of award (In Rs)	Name of Contractor	Authority approving the Contract	Final date of completion of project	Major Activities	Date of completion	Stage of completion	% of completion	Remarks
EE(E) C-VI	<u>Deposit Work</u> Establishing two 33KV ESS at Kidwai Nagar (East) Sub-Station work	Technical register at page no. 05, Sr. No. 23 on dt. 19.08.15 for Rs 15,09,85,298/-	16.02.2016	10.06.2016	31.07.2016	29,59,49,800/-	M/s JSP Projects Pvt. Ltd.	Council Item No. 25(B-02) dt. 26.04.16	-	33KV GIS boards, 11KV boards, 33KV Power Transformers, 11KV Station Transformers & LT boards.	30.5.2017	-	75%	Supply of major equipment received at site. ITC work of equipments for ESS-I is in progress. ITC work of equipments for ESS-II shall be started after completion of building of ESS-II which is being constructed by M/s NBCC.
	<u>Deposit Work</u> Establishing two 33KV ESS at Kidwai Nagar (East) SH: Supplying, Laying, Testing & Commissioning of 33KV, 400Sq.mm/3c, XLPE cable for 33KV ESS at Kidwai Nagar (East) Feeders work	Technical register at page no. 05, Sr. No. 24 on dt. 19.08.15 for Rs 6,56,86,300/-	16.02.2016	14.06.2016	31.07.2016	10,64,15,850/-	M/s Universal Cables Ltd.	Council Item No. 24(B-01) dt. 26.04.16	-	33KV HT Cable & its laying, testing & commissioning.	30.05.2017	-	80%	33KV Cable received. Three feeders out of total 5 nos. feeders have been laid. Cable laying work stopped due non availability of cable trenches which was provided by M/s NBCC.
	Supply, Installation, Testing & Commissioning 66/11KV, 16/20MVA Power Transformers & 33/11KV, 16/20MVA Power Transformer at various ESS of NDMC.	5(B-10) dt.27.08.2014 & 18(B-4) dt.09.07.2014 Technical register at page no. 07, Sr. No. 30 on dt. - 05.09.16 for Rs 5,15,00,000/-	19.10.2016	23.03.2017	29.04.2017	5,11,00,000/-	M/s Capital Electech Pvt. Ltd.	Council Item No. 09(B-24) dt. 16.01.17	-	SITC of 66/11KV, 16/20MVA & 33/11KV, 16/20MVA Power Transformers	28.12.2017	-	70%	All three power Transformer has been received at sites. Testing work of 66/11KV PTR for Vidyut Bhawan & 33/11KV PTR for Shahjahan Road is in progress

EE(E)C-VI

AEE(C-VI)

JEE(C-VI)



Sl. No.	ACTIVITY	RESPONSIBLE AGENCY	Jul-16				Aug-16				Sep-16				Oct-16				Nov-16				Dec-16				Jan-17				Feb-17				Mar-17				Apr-17				May-17				Jun-17				Jul-17				Aug-17				Sep-17				Oct-17				Nov-17				Dec-17			
			IN WEEK	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4																							
14	RECEIPT OF PAYMENT AGAINST SUPPLY & ERECTION	NDMC	P																																																																							
			A																																																																							
15	HANDING OVER OF SUB STATIONS	JSP	P																																																																							
A	KIDWAI NAGAR-EAST-I		P																																																																							
B	KIDWAI NAGAR-EAST-II		P																																																																							
			A																																																																							

NOTE: 1. CRP panel along with 11kv AIS Panels & 33 kv GIS Equipments has been installed at ESS-1






### PROJECT BAR CHART

**CUSTOMER : NDMC**

**CONTRACTOR: UNIVERSAL CABLES**

**TOTAL TIME OF COMPLETION: 10 MONTHS**

ORDER REF: D-295/EE(E) C-VI. Dt 14.06.2016

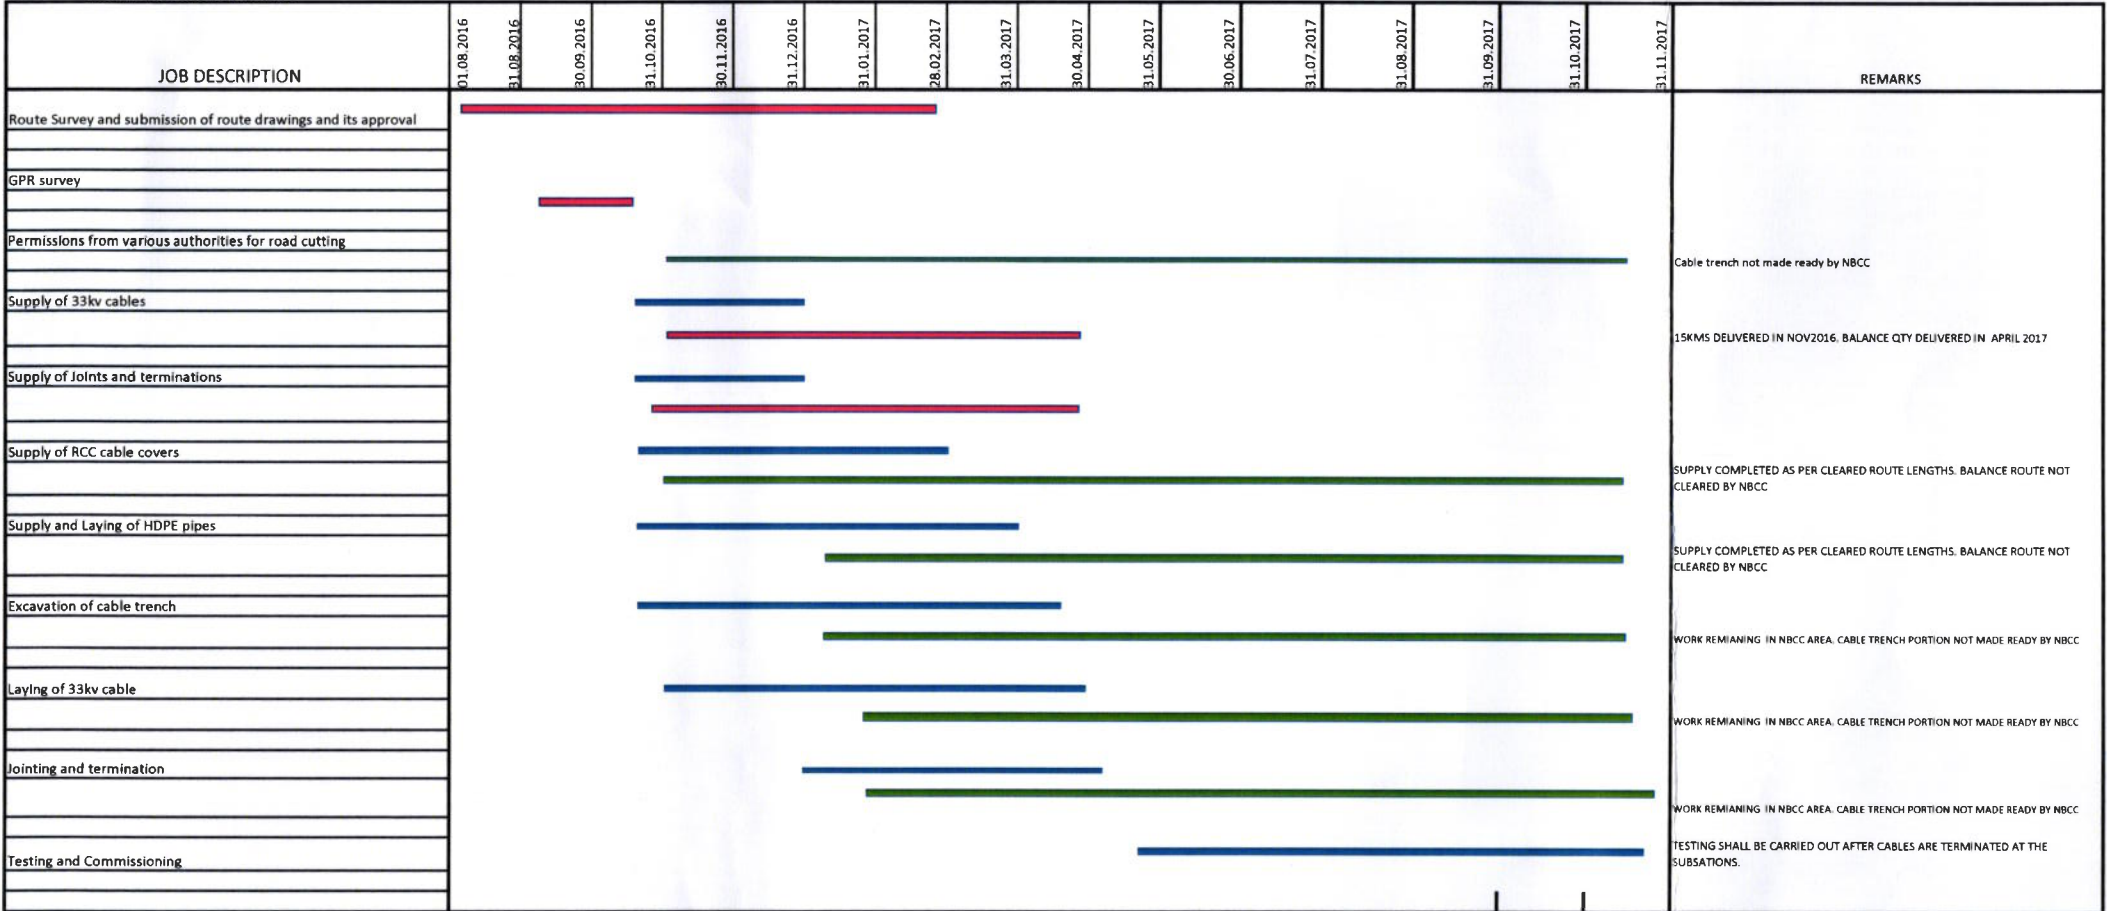

DATE: NOV 10- 2017

- █ PLANNED WORK
- █ WORK IN PROGRESS
- █ WORK COMPLETED

FOR UNIVERSAL CABLES
