

PROGRESS REPORT OF WORK ON GOING SCHEME/MORE THAN 200 LAKHS FOR THE MONTH OF JULY -2017

Name of Division	Name of work	Date of AA/ES	Date of Publishing Tender	Date of Award	Date of Start of work	Value of Award	Name of the contractor	Authority approving the contract	Final date of completion of project	Major Activities	Date of completion	Stage of completion	% of completion	Remark
1	2	3	4	5	6	7	8	9	10	11	12	13		14
EE(E) C-VI	Establishing two 33KV ESS at Kidwai Nagar Sub- Station work	Technical register at page No.05, Sr. No.23 on dt.19.08.15 for Rs.15,09,85,298/-	16.02.16	10.06.16	31.07.16	29,59,49,800/-	M/s. JSP Projects Pvt. Ltd.	Council item No.-25(B-02) dt 26.04.16	-	33KV GIS boards, 11KV boards, 33KV Power, Transformers 11 KV Station Transformers & LT Boards.	30.05.17	-	75%	Supply of major equipment received at site Due to non completion of 33KV ESS-II building which was under construction work of ESS-I, the Electrical equipment installation work stopped & it will be started after completion of work by M/s. NBCC.
EE(E) C-VI	Establishing two 33KV ESS at Kidwai Nagar(East) SH: Supplying, Laying, Testing & Commissioning of 33KV, 400Sq.mm/3c, XLPE cable for 33KV ESS at Kidwai Nagar(East) Feeders work	Technical register at page No.05, Sr.No-24 on dt.19.08.15 for Rs. 6,56,86,300/-	16.02.16	14.06.16	31.07.16	10,64,15,850/-	M/s. Universal Cables Ltd.	Council item No-24(B-01) dt.26.04.16	-	33KV HT Cable & its laying, testing & commissioning	30.05.17	-	80%	Cable laying work stopped due non availability of cable trenches which was provided by M/S. NBCC & road cut permission for Ring Road near AIIMS not granted by GAIL & PWD.
EE(E) C-VI	Supply, Installation, Testing & Commissioning 66/11KV, 16/20MVA	5(B-10) dt.27.08.2014 & 18(b-4) dt. 09.07.2014 Technical register at page No. 07,	19.10.16	23.03.17	29.04.17	5,11,00,000/-	M/s. Capital Electech Pvt. Ltd.	Council item No-09(B-24) dt.16.01.17	-	SITC of 66/11 KV 16/20 MVA & 33/11 KV, 16/20 MVA Power Transformers	28.12.17	-	50%	Issue LOC to the firm vide D-171/EE(C-VI)E dt.19.04.17 One no. 33/11 KV, 16/230 MVA

	Power Transformers & 33/11 KV, 16/20 MVA Power Transformer at various ESS of NDMC	Sr.No. 30 on dt.05.09.16 for Rs.5,15,00,000/-												& one no. 66/11KV, 16/20 MVA transformers for ESS Shahjahan Road & ESS Vidyut Bhawan delivered by the firm.
EE(E) M/F	Name of Work- Construction of under pass including corridor development works and inrersection development at the junction of Benito Juarez Marg and Inner Ring Road. SH: Shifting of HT(66KV) 630 sq.mm. Single core XLPE Cables for Construction of B.J. Marg, San Martin Marg, Ring Road Service lane Underpass (Deposit Work)	Council Resolution vide item No. 128 (B-02) Dated 12.06.2015	12.02.2016	15.02.17	24.02.17	5,00,22,613/-	M/s. Universal Cables Limited	Council	22.08.17	HT(66KV) 630 Sq.MM. Single Core XLPE Cable Laying & Jointing etc.	22.08.17	Cable Laying Work is completed and Jointing work is on progress	88%	

C.E.(E-II)

Checked
21/08/17
E.E.(T-II)

21/8/17
Sr.Asstt.(T-II)

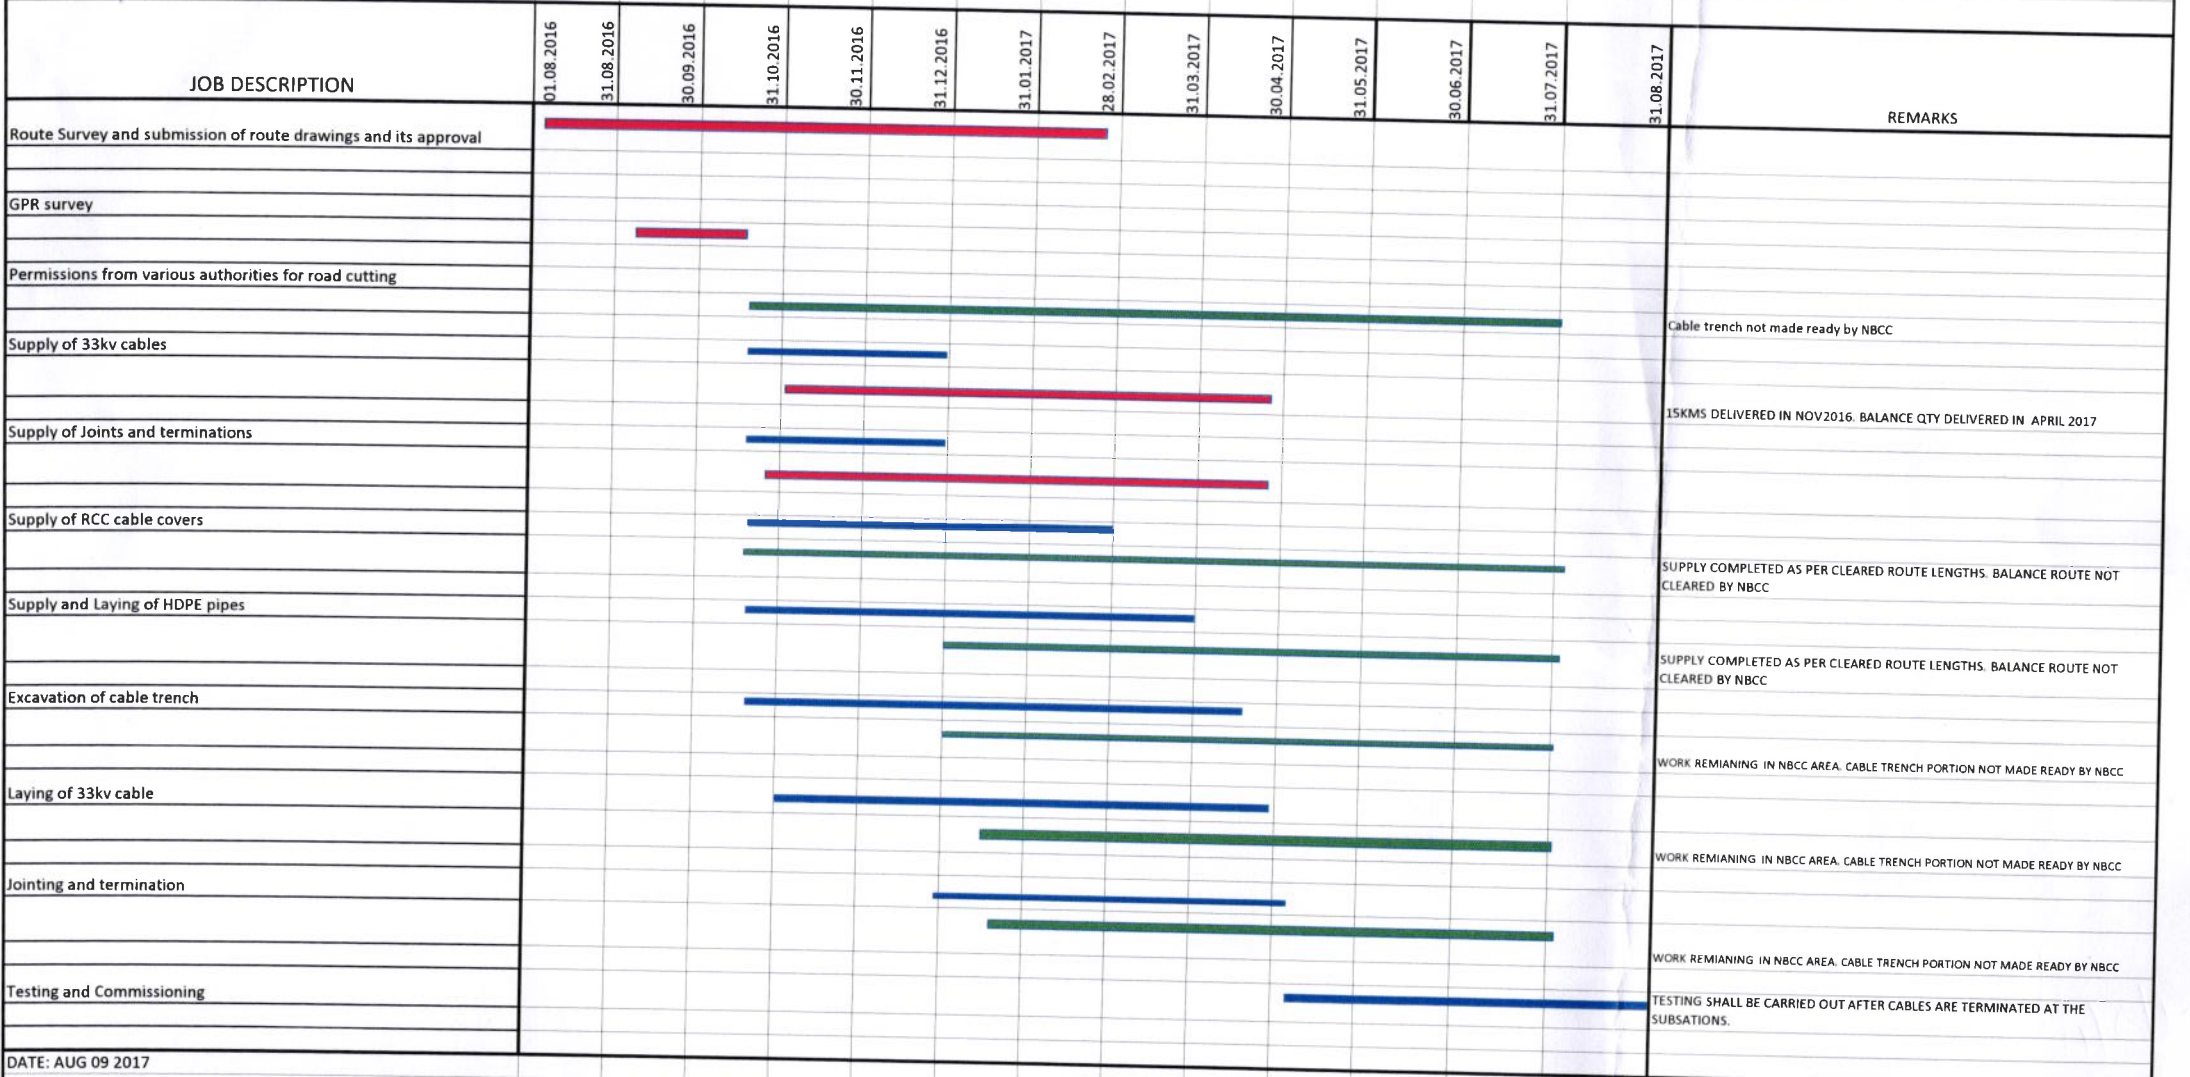
PROJECT BAR CHART

CUSTOMER : NDMC

CONTRACTOR: UNIVERSAL CABLES

TOTAL TIME OF COMPLETION: 10 MONTHS

ORDER REF: D-295/EE(E) C-VI. Dt 14.06.2016



DATE: AUG 09 2017

FOR UNIVERSAL CABLES

- PLANNED WORK
- WORK IN PROGRESS
- WORK COMPLETED

PROJECT- SITC OF ONE 66/11 KV, 16/20 MVA POWER TRANSFORMER & TWO NOS. 33/11 KV 16/20 MVA POWER TRANSFORMERS AT VARIOUS ESS OF NDMC
 CUSTOMER: NDMC
 LOI NO. :D-176/EFIC-VIJE DT. 28/03/17
 TENDER ID NO. :2016_NDMC_116484_1

BAR CHART

M/S CAPITAL ELECTECH PVT. LTD. GHAZIABAD

P	Planned Schedule
A	Activity Completed
PR	Activity under Progress



PROJECT BAR CHART



CUSTOMER : NDMC

CONTRACTOR: UNIVERSAL CABLES

TOTAL TIME OF COMPLETION: 06 MONTHS

LOA REF: D-149/EE (M/F)/2016-17 Date: 31.01.2017

PHYSICAL PROGRESS BAR CHART as on 31.07.2017

JOB DESCRIPTION	14.02.2017	28.02.2017	11.03.2017	30.04.2017	31.05.2017	30.06.2017	31.07.2017	22.08.2017	REMARKS
Route Survey and its approval	[Solid blue bar from 14.02.2017 to 28.02.2017]								ACTIVITY COMPLETE
Submission of drawings and its approval	[Solid blue bar from 14.02.2017 to 28.02.2017] [Dashed blue bar from 14.02.2017 to 20.04.2017]								ACTIVITY COMPLETE Drawings approved on 20.04.2017
Permissions from various auth for excavation/ road cutting	[Dashed blue bar from 11.03.2017 to 20.04.2017]								ACTIVITY COMPLETE Permission to excavate received 1st week of May
Supply and Laying of HDPE pipes by HDD/Boggy method	[Solid blue bar from 30.04.2017 to 30.06.2017] [Dashed blue bar from 30.04.2017 to 30.06.2017]								ACTIVITY COMPLETE
Manufacturing & supply of 66kv cables	[Solid blue bar from 11.03.2017 to 30.04.2017] [Dashed blue bar from 11.03.2017 to 30.04.2017]								ACTIVITY COMPLETE
Manufacture and delivery of Joints and terminations	[Solid blue bar from 11.03.2017 to 30.06.2017] [Dashed blue bar from 11.03.2017 to 30.06.2017]								ACTIVITY COMPLETE
Supply of RCC cable covers	[Solid blue bar from 11.03.2017 to 30.06.2017] [Dashed blue bar from 11.03.2017 to 30.06.2017]								ACTIVITY COMPLETE
Excavation of cable trench	[Solid blue bar from 30.04.2017 to 30.06.2017] [Dashed blue bar from 30.04.2017 to 30.06.2017]								ACTIVITY COMPLETE
Laying of 66kv cable	[Solid blue bar from 30.04.2017 to 30.06.2017] [Dashed blue bar from 30.04.2017 to 30.06.2017]								ACTIVITY COMPLETE
Jointing and termination	[Solid blue bar from 31.05.2017 to 31.07.2017] [Red hatched bar from 31.05.2017 to 31.07.2017]								In progress
Testing and Commissioning	[Solid blue bar from 31.07.2017 to 22.08.2017]								Will be done after completion of joints
	<div style="display: flex; justify-content: space-between;"> <div style="width: 20%;">FOR UNIVERSAL CABLES</div> <div style="width: 60%; text-align: center;">  </div> <div style="width: 20%; text-align: right;">  </div> </div>								
